



**thompson**  
CONSULTING SERVICES

# DEBRIS COLLECTION PROGRESS REPORT

Progress Through: 3/30/2014

Client: Aiken County, SC

Project: Winter Storm Pax Debris Removal


Report Generated On: 3/31/2014

## Project Collection Estimates

**Estimated ROW CY: 600,000      Estimated LHS Count: 100,000**

## Right of Way (ROW) Progress Chart

**Project to Date CY: 554,496**

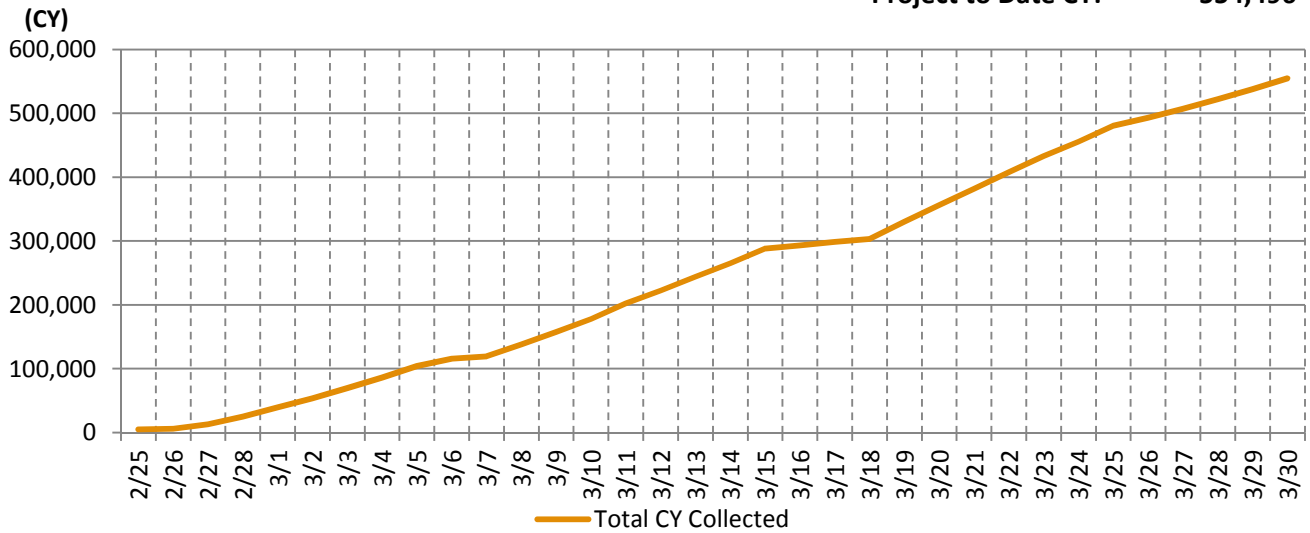

## Leaner / Hanger / Stump (LHS) Progress Chart

**Project to Date Count: 92,057**

